


CCNP - Project Schedule v4

ID	Task Name	Duration	Start	Finish	2019												2020												2021											
					M	T	W	T	F	S	S	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	
1	Tasks 1-4: Neighborhood Parks	615 days	Mon 6/24/19	Fri 10/29/21																																				
2	Task 1 - Project Coordination	0 days	Wed 7/24/19	Wed 7/24/19																																				
3	Project Kick Off Meeting	0 days	Wed 7/24/19	Wed 7/24/19																																				
4	Task 2 - Planning and Site Assessment	115 days	Mon 6/24/19	Mon 12/2/19																																				
5	Site Assessment and Analysis	115 days	Mon 6/24/19	Fri 11/29/19																																				
6	Public Engagement Workshops	3 days	Tue 9/17/19	Thu 9/19/19																																				
7	Plan Refinements	36 days	Fri 9/20/19	Fri 11/8/19																																				
8	City Review of Final Concepts	10 days	Mon 11/11/19	Fri 11/22/19																																				
9	City Council Presentation (Approval)	0 days	Mon 12/2/19	Mon 12/2/19																																				
10	Task 3 - Design, Permitting and Bidding	345 days	Mon 10/28/19	Fri 2/19/21																																				
11	30% Design and Cost Estimate Prep	60 days	Mon 12/2/19	Fri 2/21/20																																				
12	30% Design Review Meetings and Refine	20 days	Mon 2/24/20	Fri 3/20/20																																				
13	60% Design Prep and Cost Estimate Update	55 days	Mon 3/23/20	Fri 6/5/20																																				
14	60% Design Review Meetings and Refine	15 days	Mon 6/8/20	Fri 6/26/20																																				
15	Final Design and Permitting Package Prep	30 days	Mon 6/29/20	Fri 8/7/20																																				
16	City Council Approval of Final Design	20 days	Mon 8/10/20	Fri 9/4/20																																				
17	Permit Coordination / Pre-App Mtgs	225 days	Mon 10/28/19	Fri 9/4/20																																				
18	Permit Submittals and Approvals *	60 days	Mon 9/7/20	Fri 11/27/20																																				
19	Bid Solicitation	60 days	Mon 10/5/20	Fri 12/25/20																																				
20	Contractor Selection / Council Approval	40 days	Mon 12/28/20	Fri 2/19/21																																				
21	Task 4 - Construction Phase Services	180 days	Mon 2/22/21	Fri 10/29/21																																				
22	Site Prep, Demo, Grading, Utilities *	40 days	Mon 2/22/21	Fri 4/16/21																																				
23	Paving and Concrete	60 days	Mon 4/19/21	Fri 7/9/21																																				
24	Structures and General Building	60 days	Mon 5/17/21	Fri 8/6/21																																				
25	Power/Electrical, Communications	30 days	Mon 6/28/21	Fri 8/6/21																																				
26	Amenities and Landscape	30 days	Mon 8/9/21	Fri 9/17/21																																				
27	Neighborhood Parks Grand Openings	30 days	Mon 9/20/21	Fri 10/29/21																																				
28	Task 5: Design/Eng. of Shade Structures	330 days	Mon 6/24/19	Fri 9/25/20																																				
29	Planning and Site Assessment	160 days	Mon 12/9/19	Fri 7/17/20																																				
30	Site Assessment (Football after 1/1/20)	50 days	Mon 12/9/19	Fri 2/14/20																																				
31	Concept Development	30 days	Mon 2/17/20	Fri 3/27/20																																				
32	Bid Solicitation	50 days	Mon 3/30/20	Fri 6/5/20																																				
33	Contractor Selection	30 days	Mon 6/8/20	Fri 7/17/20																																				
34	Design and Permitting	100 days	Mon 7/20/20	Fri 12/4/20																																				
35	60% Construction Documents	30 days	Mon 7/20/20	Fri 8/28/20																																				
36	60% Review Meeting and Refine	20 days	Mon 8/31/20	Fri 9/25/20																																				
37	Final Construction Documents	20 days	Mon 9/28/20	Fri 10/23/20																																				
38	Permit Submittals and Approvals *	30 days	Mon 10/26/20	Fri 12/4/20																																				
39	Construction Phase Services	110 days	Mon 12/7/20	Fri 5/7/21																																				
40	Site Prep & Demo (Playgrounds and Baseball)	20 days	Mon 12/7/20	Fri 1/1/21																																				
41	Shade Structures (Playgrounds and Baseball)	50 days	Mon 1/4/21	Fri 3/12/21																																				
42	Site Prep & Demo (Football)	20 days	Mon 2/15/21	Fri 3/12/21																																				
43	Shade Structures (Football)	40 days	Mon 3/15/21	Fri 5/7/21																																				

City of Cape Coral

Community Parks - Overall Project Schedule
(shown in calendar days)

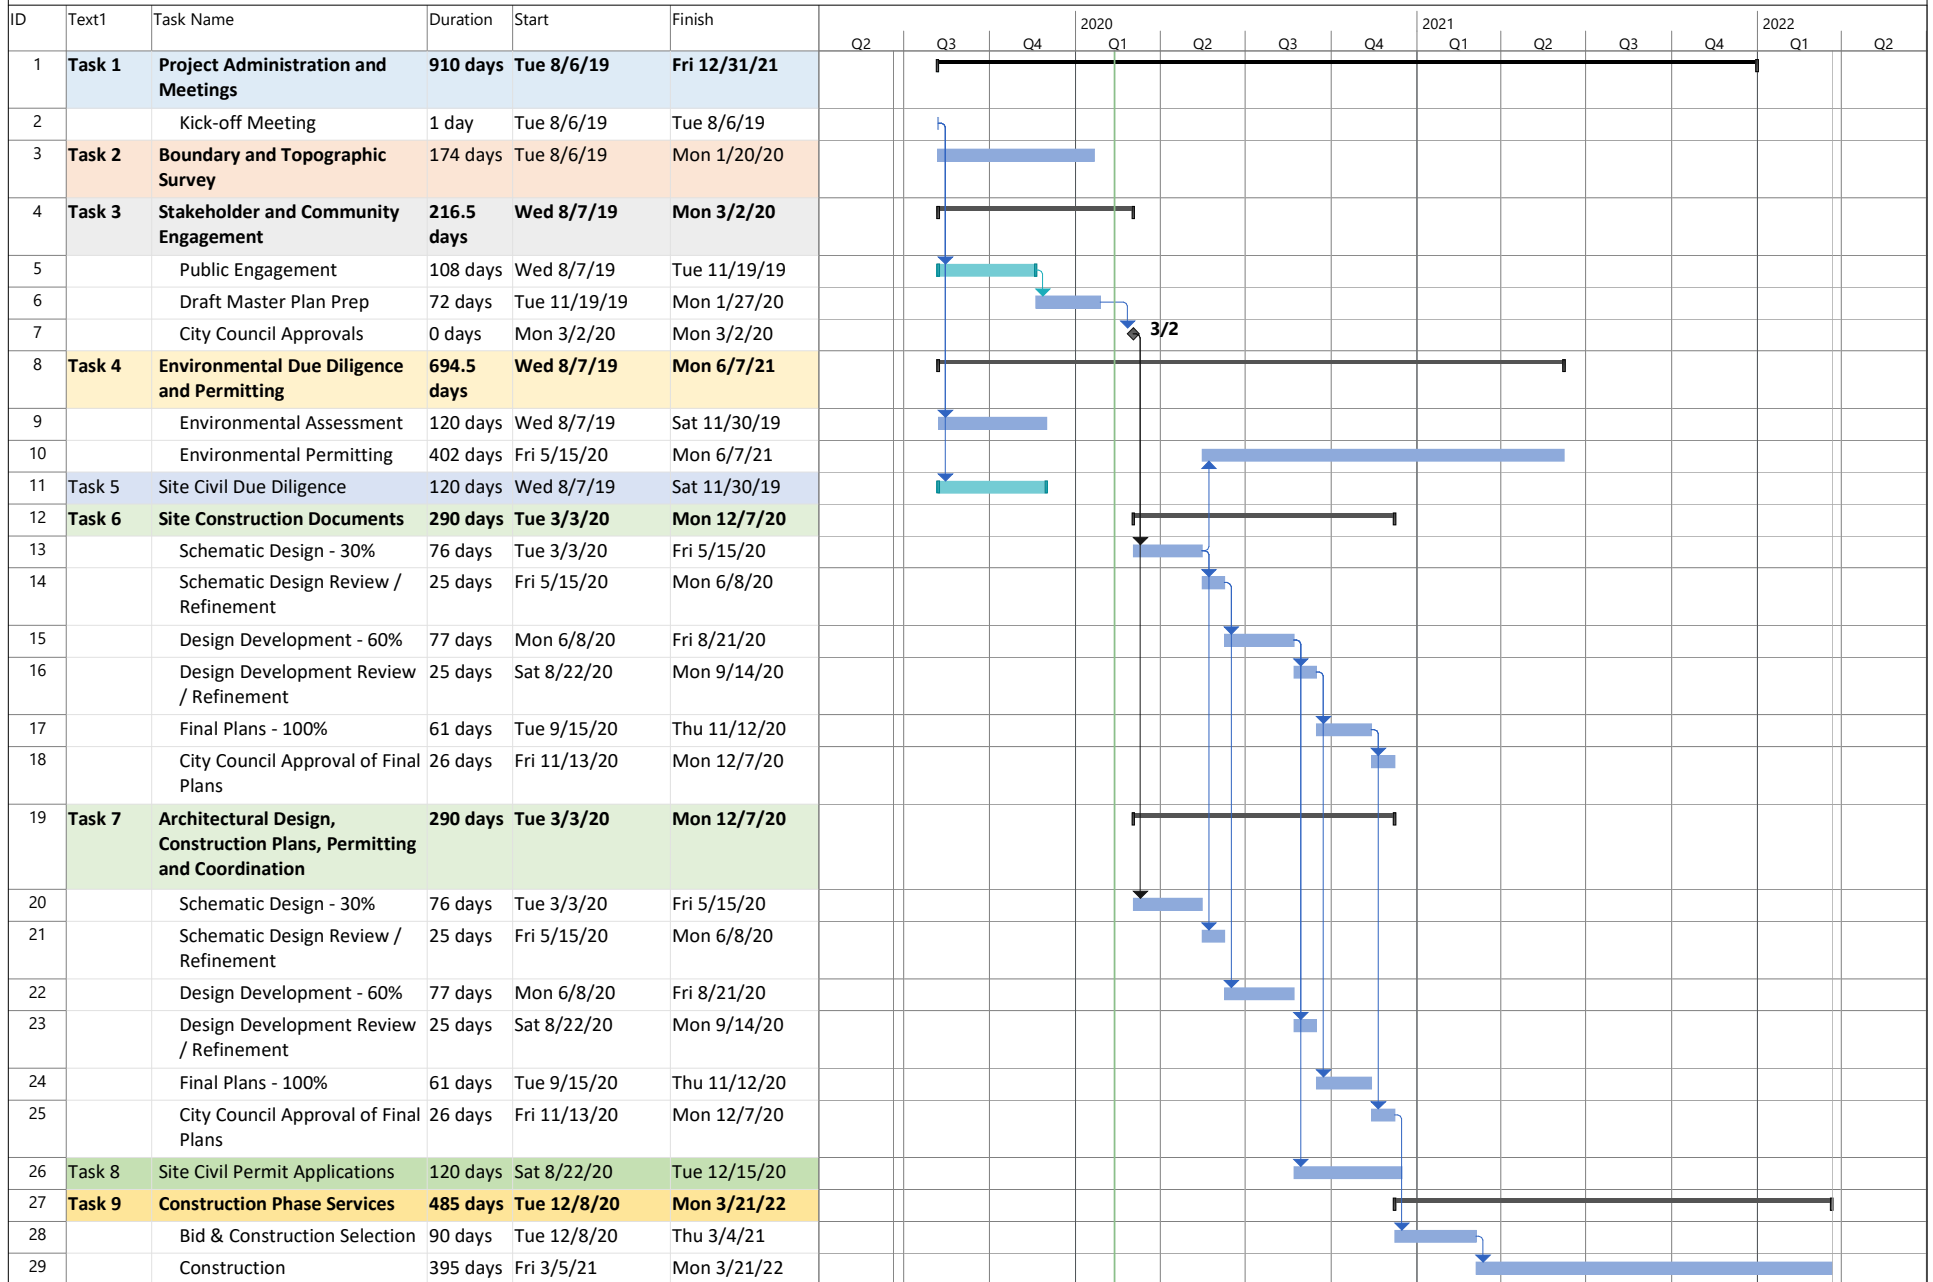

Note: Yacht Club will have its own schedule with timeline to be determined.
